# CMAP CONSTRUCTION COORDINATION



Will County FY 2015

## BUILD WILL UPDATE / ADDITIONAL PROJECTS

- 2008-Present
  - 83 projects on County Highway System
    - 72 Build Will
    - 11 Additional
  - \$483 million program
    - Approximately \$120 Million Completed through 2014
  - Funded with
    - RTA sales tax
    - Federal, State, & other Local funding sources
    - \$100 million in bonds approved by County Board
- 2015
  - Bond Expenditures Complete
  - Major Revenue : RTA & MFT Funds



#### **UPDATE** (cont.)

- Largest Overlay Program in History
  - Last 5 Years
    - 162 Center-line Miles
    - 59 County Highways
  - FY 2015
    - 16 Center-line Miles
    - 9 County Highways
  - 6 Year Total
    - 178 Center-line Miles
    - 68 County Highways





#### **FY 2015 PROGRAM**

**Road Construction** 

Structure Rehab & Reconstruction

Engineering (Phases I, II, & III)

**ROW Acquisition** 


Build Will + Additional Projects Total and \$88.2 million



#### **PROGRAM HIGHLIGHTS**

- I-55 @ Weber Road Phase II Engineering underway,
  Construction tentatively scheduled for 2016
- 95<sup>th</sup> Street @ Plainfield-Naperville Road Tentative Letting Scheduled April 2015
- 135<sup>th</sup> Street: New to Smith Tentative Letting Scheduled May 2015
- Bell Road (159<sup>th</sup> Street 151<sup>st</sup> Street and at 143<sup>rd</sup> Street) *Tentative Lettings Scheduled June and September 2015, respectively*


#### I-55 AT WEBER ROAD

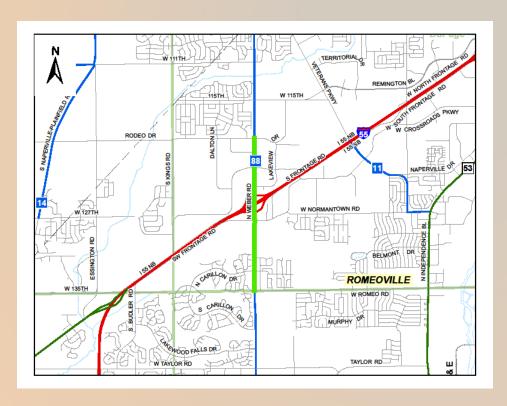

- Scope
  - New Interchange
  - Add Lanes
  - IntersectionImprovements
- Funding: State, County, & Local Funds
- Design:
  - Currently in 2 projects
  - 119<sup>th</sup> to Normantown
    & Normantown to
    135<sup>th</sup>
- Construction Tentatively
  Scheduled to begin in 2016

#### 95TH STREET AT PLAINFIELD-NAPERVILLE ROAD

- Scope
  - Noise Walls
  - Dual Left Turn Lanes
  - Right Turn Lanes
  - Structure Reconstruction
- Funding: Approx. Federal Funds (STR)
- Tentative Letting:
  April 2015

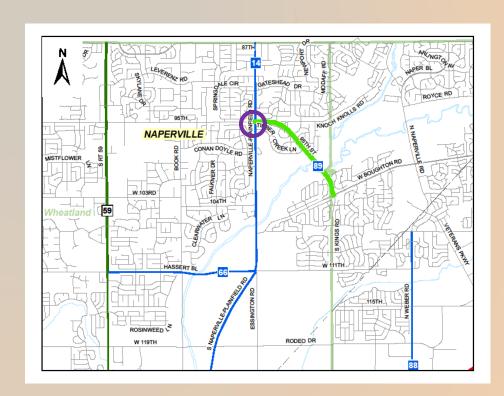



#### 135<sup>TH</sup> STREET

Smith Road to New Avenue

Project Length: 1.3 miles

- Project Scope:
  - Roadway Reconstruction
  - Add Lanes (4 Lane)
- Tentative Letting: May 2015

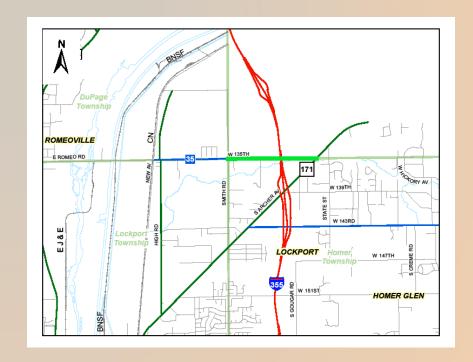

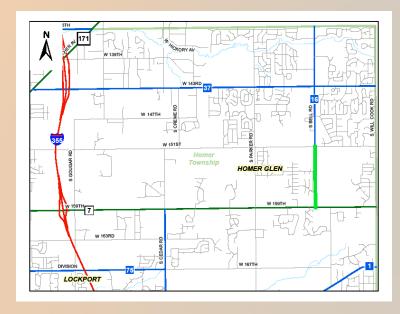



#### **BELL ROAD**

- · 159th Street to 151st Street
- Project Length: 1.0 miles
- Project Scope:
  - Roadway Reconstruction
  - Add Lanes (4 Lane)
- Tentative Letting: June 2015
- · At 143rd Street
- Project Scope: Project Scope:
  - Intersection Reconstruction
  - Traffic Signals
  - Turn Lanes
  - Add Lanes (4 Lane on 143<sup>rd</sup>
    St and 6 Lanes on Bell Rd)
- Tentative Letting: September
  2015

#### **JOB CREATION & RETENTION**

- According to US Department of Transportation
  - 1 job-year created
  - Per \$92,000 in Government
    Expenditures
- Build Will FY 2015 Creates:
  959 job-years



### QUESTIONS?
